

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 7/26/2026



For Project: **Indian Springs Sewer Phase 2B**
NFWFMD Const. Grant Agreement No. 20-036 AHE # 20-033
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell Engineering Inspector: Dwayne Josey (850) 258-3386
Notice to Proceed: 8/1/2023 Award Date: 1/24/2023

Substantial Completion: 2/2/2026

Final Completion: 4/3/2026

The report is for the week of: Monday, 7/20/2026

thru Sunday, 7/26/2026

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- No work at contractor's option.

Tuesday- No work due to rain. Rain day granted.

Wednesday- Installed sst junction box at Wayside lift station.

Thursday- No work at contractor's option.

Friday- No work at contractor's option.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.


Engineer's remarks/Pending issues:

Percent Project Complete:	95%	Time Remaining (%):	-14%
Invoiced to Date:	\$5,001,931.28	Weather days to date:	45
Original Contract Amount:	\$6,377,639.99	Holiday days granted:	67
Change Order Amount Approved:	\$262,722.00	Actual Days:	1091
Contract Time Approved:	504	Days used with deduct:	979
Remaining:	\$1,638,430.71		
Days to Substantial Completion:	804 Original SC:	300 Remaining to SC:	-175
Days to Final Completion:	864 Original FC:	360 Remaining to FC:	-115


Approved: Robin G. Besczeynski, Utility Project Manager (850-526-2040)
Completed on lot connection: 24
Completed septic tank abandoned: 24

South East Elevation

☉ 329°NW (T) ☉ 30°45'20"N, 85°11'45"W ±4m ▲ 26m (MSL)

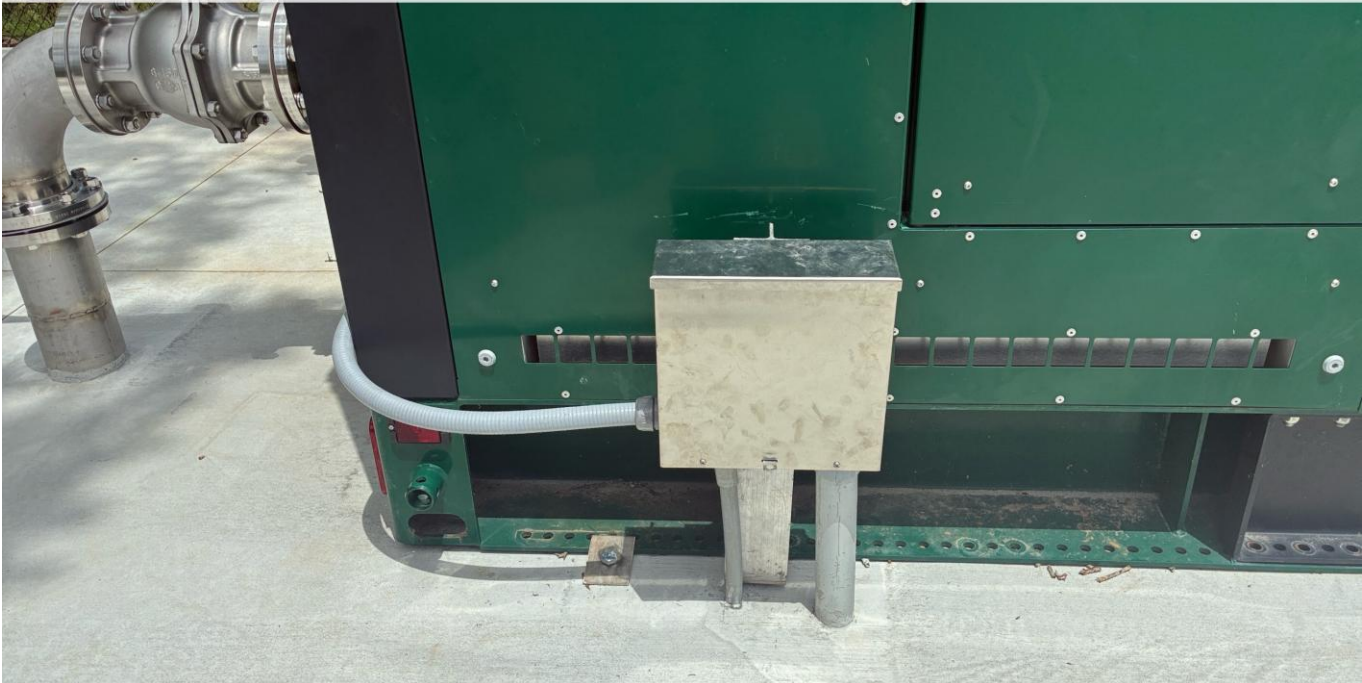

South West Elevation

☉ 32°NE (T) ☉ 30°45'20"N, 85°11'45"W ±5m ▲ 27m (MSL)



Wayside

Indian Springs phase 2B
22 Jul 2026, 11:48:01 AM
