

CEI WEEKLY SUMMARY OF EVENTS, OBSERVATIONS AND REMARKS

Prepared for: Jackson County, FL
Prepared by: Alday-Howell Engineering, Inc.
Prepared on: 8/16/2026
For Project: **Indian Springs Sewer Phase 2D**
NWFWMD Const. Grant Agreement No. 20-036 AHE # 23-012
Contractor: Blankenship Contracting, Inc.
Designer: Alday-Howell, Engineering Inspector: Dwayne Josey 850-258-3386
Notice to Proceed: 11/4/2024 Award Date: 12/13/2022



Substantial Completion: 1/1/2027

Final Completion: 3/2/2027

The report is for the week of: Monday, 8/10/2026

thru Sunday, 8/16/2026

The contractor performed the following operations this week. Sub work is noted in parenthesis:

Monday- Made field changes to compensate for utility conflict.

Tuesday- Precut asphalt on Oak Dr.

Wednesday- Installed 28 lf of 8" gravity on Oak Dr.

Thursday- Installed 56 lf of 8" gravity on Oak Dr.

Friday- Cleaned and repaired road on Oak Dr.

Saturday- No work at contractor's option.

Sunday- No work at contractor's option.

Engineer's remarks/Pending issues: Percent complete is phase specific, invoiced is per project.


Percent Project Complete:	16%	Time Remaining (%):	20%
Invoiced to Date:	\$4,085,928.19	Weather days to date:	41
Original Contract Amount:	\$6,168,668.47		
Change Order Amount Approved:	\$2,820,626.04	Holiday days granted:	47
Contract Time Approved:	400	Actual Days:	651
Remaining:	\$4,903,366.32	Days used with deduct:	563
Days to Substantial Completion:	700 Original SC:	300 Remaining to SC:	137
Days to Final Completion:	760 Original FC:	360 Remaining to FC:	197

Completed on lot connection: 0
Completed septic tank abandoned: 0

Approved:  Robin G. Besczezynski, Utility Project Manager (850-526-2040)

South West Elevation

☼ 47°NE (T) ● 30°46'20"N, 85°9'45"W ±2m ▲ 50m (MSL)

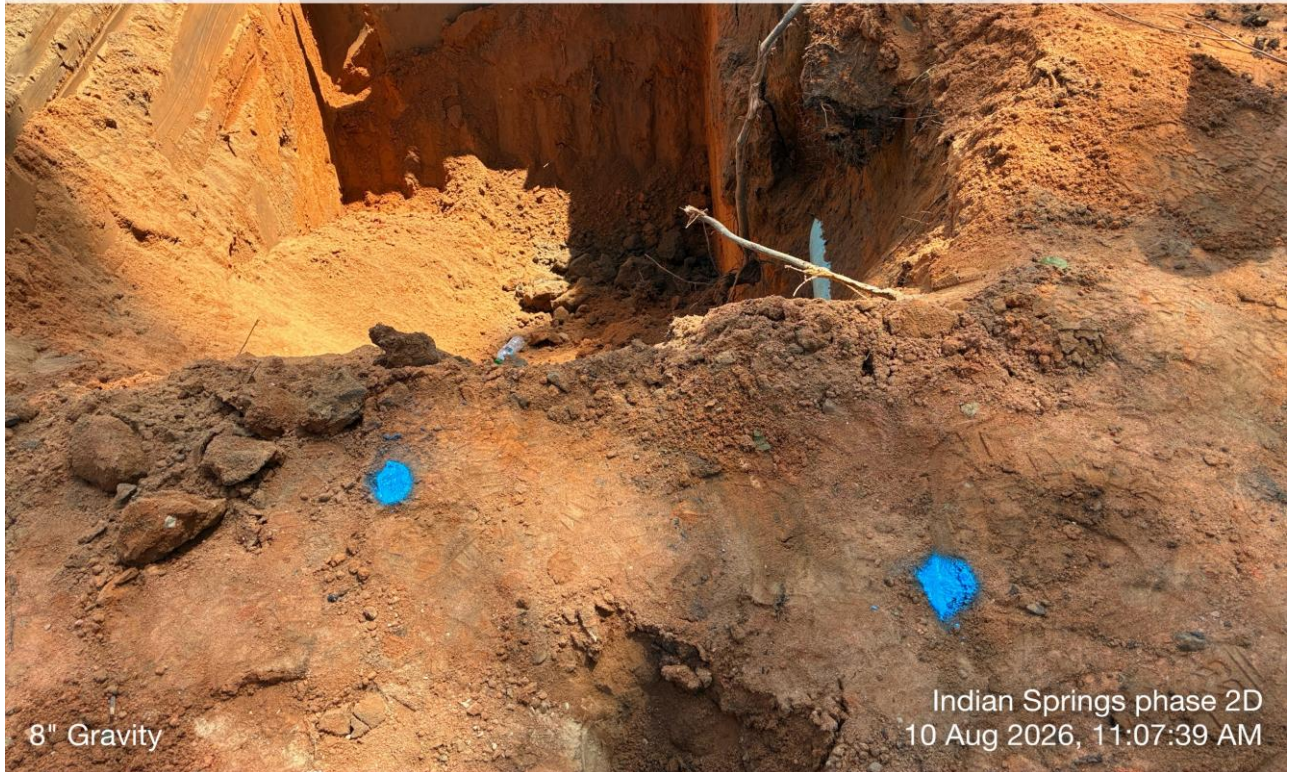

8" Gravity

Indian Springs phase 2D
10 Aug 2026, 11:07:39 AM

NORTH EAST ELEVATION

☼ 227°SW (T) ● 30°46'21"N, 85°9'44"W ±2m ▲ 53m (MSL)



8" Gravity

Indian Springs phase 2D
13 Aug 2026, 8:08:34 AM

North East Elevation

☼ 243°SW (T) ● 30°46'21"N, 85°9'44"W ±3m ▲ 53m (MSL)

